



# Fort Wayne Riverfront Phase 1 Park Foundation Pavilion



## Weekly Progress Update for Week Ending 1/13/19

### Past Week of Progress

- |  |  |
|--|--|
| <ul style="list-style-type: none"> <li>* Continue on T&amp;G Cedar Ceiling Within Park Foundation Pavilion Event Space</li> <li>* Start Installation of Pre-Finished Metal Wall System at East Canopy Skylights</li> <li>* Install Acoustical Ceiling Grid Within the Pavilion Event Space</li> <li>* Excavate, Place Dumpster Bollards, and Pour Concrete at Base and In Bollard</li> </ul> | <ul style="list-style-type: none"> <li>* Continue Exterior Canopy T&amp;G Cedar Soffit and Around Exterior Restroom Entrances</li> <li>* Start Installation of Restroom Partitions In Pavilion Interior Event Space Bathrooms</li> <li>* Install HVAC Duct Work Within Pavilion Event Space Acoustical Ceiling Grid</li> <li>* Install Lighting Fixtures Within Event Space Acoustical Ceiling Grid</li> </ul> |
|--|--|


### Next Week Look Ahead

- |   |  |
|---|--|
| <ul style="list-style-type: none"> <li>* Complete T&amp;G Cedar Ceiling Within Park Foundation Pavilion Event Space</li> <li>* Continue Installation of Pre-Finished Metal Wall System at East Canopy Skylights</li> <li>* Start Installation of Sprinkler Heads/Escutcheons Within Pavilion Exterior Canopy</li> </ul> | <ul style="list-style-type: none"> <li>* Continue Exterior Canopy T&amp;G Cedar Soffit and Around Exterior Restroom Entrances</li> <li>* Complete Installation of Restroom Partitions In Pavilion Interior Event Space Bathrooms</li> <li>* Start Drywall Touch-Ups In Areas Where Work is Substantially Complete Within Pavilion</li> </ul> |
|---|--|

### Milestone Events

- \* Week of 1/28/19 Complete Interior T&G Cedar Ceiling Within Event Space

### Park Foundation Pavilion Progress Photos

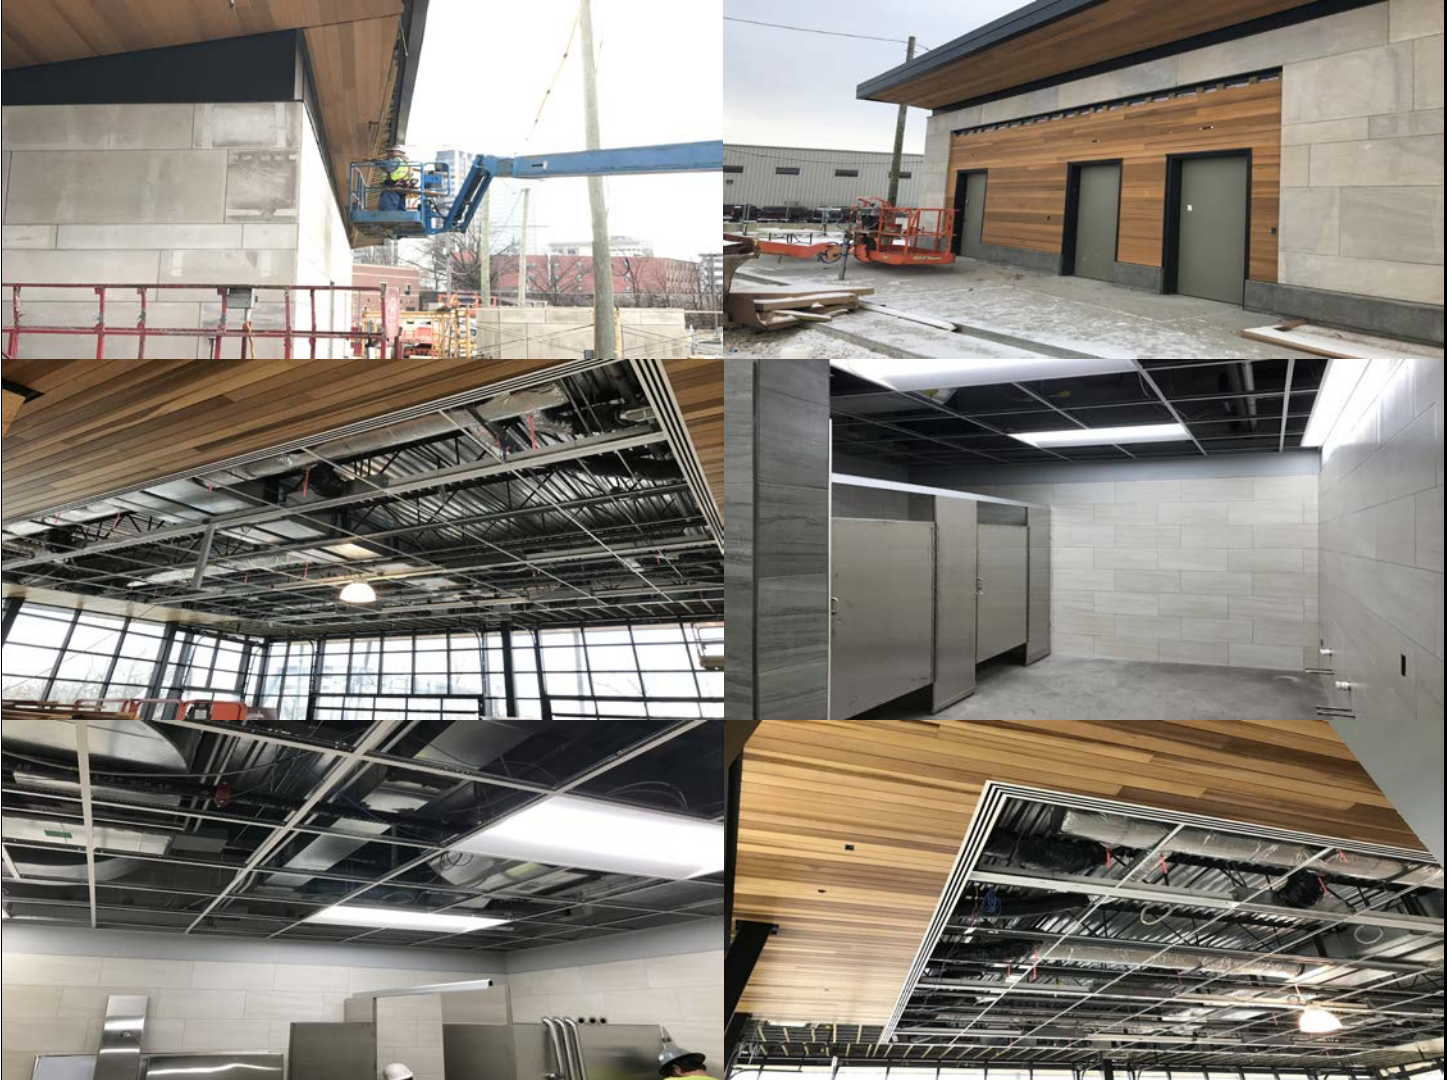





# Fort Wayne Riverfront Phase 1

## River Work North/South Shore & Misc. Site Excavation



### Weekly Progress Update for Week Ending 1/13/19

#### Past Week of Progress

- \* Continue IPE Decking on Parkview TCT Sections
- \* Backfill Behind W17 Lounger Seat Wall and W2D Seating @ Turf
- \* Pour W-2D Seat Wall @ Turf East and W-2G Foundation Wall Seating @ Turf West
- \* Excavate/Install 4" High Pressure Water Lines for Rill From Manifold to Source Boulder
- \* Layout, Excavate, & Pour Boulder Locations For Kids Canal Water Feature Foundations
- \* Pour Sections of Slab (Areas to Receive Fluid Applied) @ Kids Canal Water Feature
- \* Continue to Excavate, Prep, and Pour Kids Canal Water Feature Foundations
- \* Install Rip-Rap at West End of South Seawall
- \* Install Pavers at Superior Street ROW
- \* Form/Prep W3C and W3D Terraced Seating @ Ambassador Enterprises Amphitheatre
- \* Rough In Electrical Lines @ Ambassador Enterprises Amphitheatre Terraced Seating

#### Next Week Look Ahead

- \* Continue IPE Decking on Parkview TCT Sections
- \* Form, Prep, and Pour W3B, W3C, W3D, & W3E @ Ambassador Ent. Amphitheatre
- \* Excavate/Install Conduit Runs from Secondary Transformer to Sweetwater Bandshell
- \* Bring Up to Subgrade Kids Canal Water Feature and Continue to Pour Slab Sections
- \* Form/Prep East and West Cheek Walls @ Ambassador Ent. Amphitheatre Grand Stairs
- \* Continue Miscellaneous Site Grading

#### Milestone Events

- \* Week of 1/28/19 Start to Form, Prep, and Pour S6 Grand Stairs
- \* Week of 1/28/19 Start to Form, Prep, and Pour 12"x6" Rill Curb

#### North/South Site Progress







# Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



## Weekly Progress Update for Week Ending 1/13/19

### North/South Site Progress Photos

